



Verizon MDU Report

Install Status	May-15	Sep-14
VZ Service to Condos		
No Response	25	0%
PAL	9	-89%
In Negotiations	24	8%
Tech / Probs	12	17%
In Construction	3	67%
Video Valid	117	8%
Unaccounted	4	-100%
Total	194	
Total Accounted	190	

VZ Service to Condos

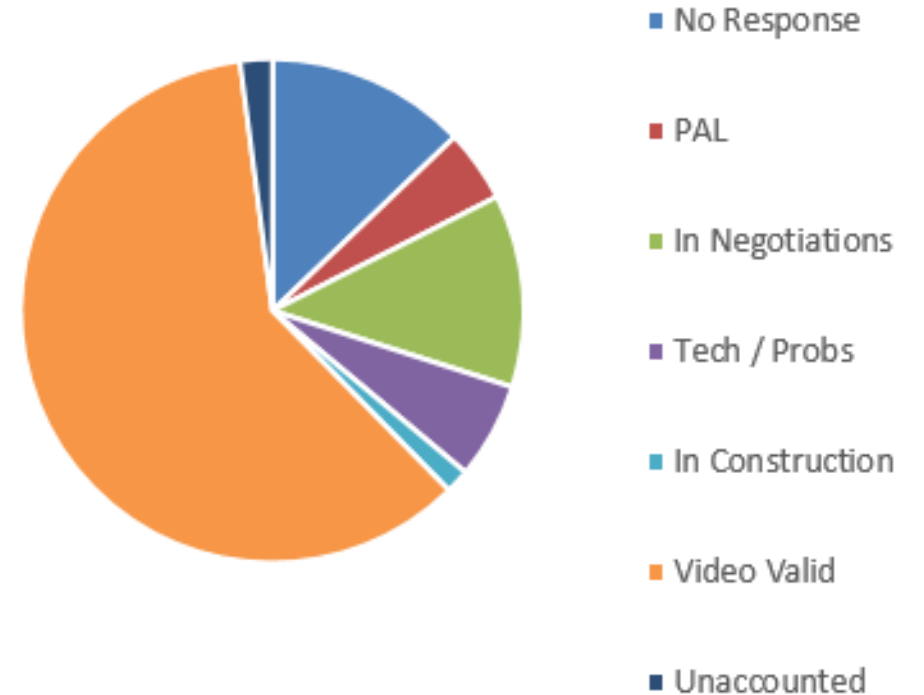

	May-15	Sep-14
VZ Service to Apts		
No Response	278	-1%
PAL	61	20%
In Negotiations	157	-18%
Tech Probs	10	-80%
In Construction	8	38%
Video Valid	308	6%
Unaccounted	46	-422%
Total	868	
Total Accounted	822	
<i>*Unaccounted are locations that have reverted or re-entered the process from PAL to Video Validated</i>		

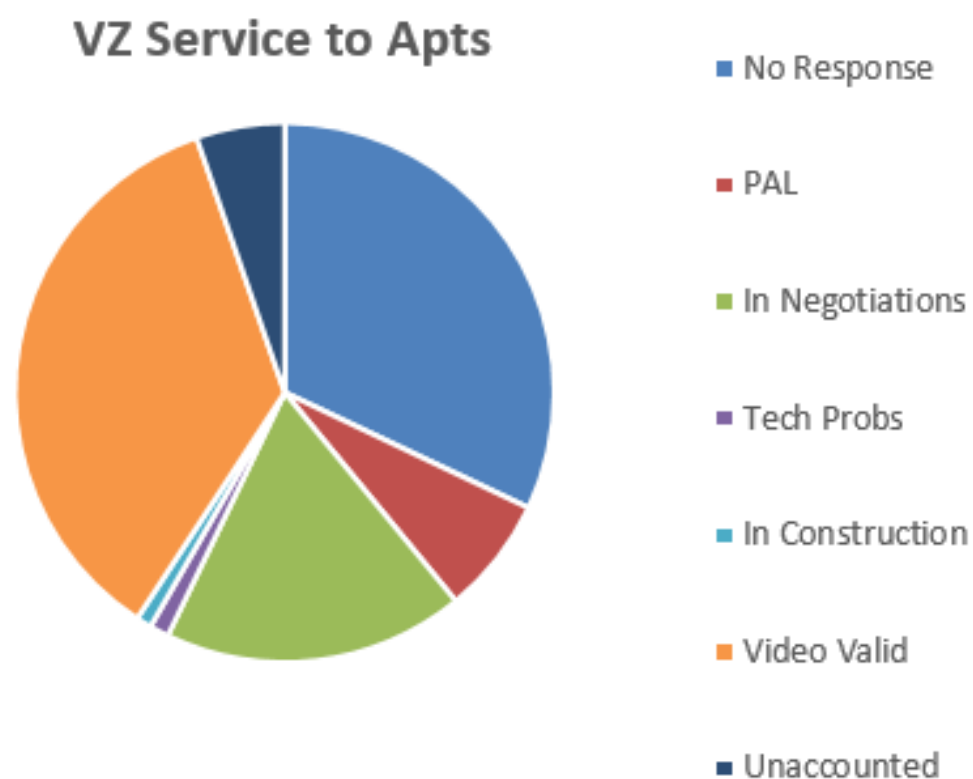

- By the time notifications are sent, FiOS is available
- When a PAL is signed or the MDU does not respond, they are in the Verizon Build Status Report
- Verizon is starting construction on the Single Family Units (SFU) Build in Crystal City, Barcroft and Alexandria Wire Centers in the 3rd Quarter of this year (Jul-Sep 2015)
- Thus Verizon expects to meet the timeline required by the Franchise Agreement
- There is a very large proportion of MDU's in this Extended Area Build -- Verizon
